

INSTALLATION OF WELL WATER RECHARGING SYSTEM AT KOPAY AND KAYTS DIVISIONS IN JAFFNA PENINSULA

Lanka Rain Water Harvesting Forum

Progress report: January – March 2026

Deliverable/Output	Due Date	Conducted Date
1. Development of criteria for the selection of beneficiary households and mobilizing them towards the successful implementation of the project	September 15, 2025	Criteria developed and beneficiaries selected.
2. Establish relationship with local agencies and obtain necessary approval	September 15, 2025	October 2 nd , 2025 Approval obtained from District Secretary Jaffna and DS Kayts and DS Kopay
3. Ensure the community contribution	September 15, 2025	Selected beneficiaries requested to install Valance Board at Kopay
4. Collection of baseline data-water depth and quality parameters	September 20, 2025	Collected from Kopay 7/11/2025
5. Installation of 20 well recharge systems	October 10, 2025	10 well recharge systems installed in Kaytes 30/12/2025 10 well recharge systems installed in Kopai 28/1/2026
6. Completion of community awareness and capacity building on operation and maintenance	October 20, 2025	Kapay on 10/2/2026
7. Submission of a brief report, baseline data, observations, photos, etc.	October 30, 2025 November- December 2025	Submitted Submitted

Details of Activity Conducted

1. Discussion with Development Officer at Kopay to reselect beneficiaries 30/12/2025
2. Beneficiaries were reselected to Install 10 well recharge system at Kopay (annex 1)
3. Completed installation of 10 well recharge systems at Kopay 28.01.2026 (annex 2)
4. Conducted Operation and maintenance training to beneficiaries on 10/2/26 (annex 3)

Constraints

- Flood situation due to Ditwah cyclone, roads not accessible and beneficiaries were affected and in safe centers
- Delay in installation of Valence board by selected beneficiaries in Kopay. The site was revisited on 30/12/2025; 3 households agreed to install the valence board by 3/1/2026. Discussion held with Development officer Kopay to reselect beneficiaries

Annex 1


Beneficiary Details of Well recharge system installed in Kopay

No	4- Name	5- Address	6- Contact no	Beneficiary details			GPS Locations	
				F	M	Total	Latitude	Longitude
1	Thankaveluitham Kugarasa	Madaththady	077 5949890	1	3	4	9.6786847	80.0600102
2	Thevaranjan Kantharaj	Madaththady	076 2562643	3	2	5	9.677542	80.0593479
3	Balasingam Saroja	Madaththady	076 8853104	4	1	5	9.6790302	80.0589264
4	Thusyanthan Renuka	Madaththady	076 6312768	4	1	5	9.6786002	80.0597475
5	Ragupathi Kala	Madaththady	076 1329725	2	4	6	9.6775452	80.05783996
6	Vasanthaselan Maliny	Madaththady	077 8449170	1	2	3	9.6818415	80.0587736
7	Kanagalingam Ramesh	Madaththady	076 9935717	1	3	4	9.6771996	80.05716248
8	Sinnathurai Santhakumar	Madaththady	-	3	3	6	9.6788421	80.0600476
9	Sivarasa Balrasa	Madaththady		4	4	8	9.6785657	80.05772284
10	Senathiraja Santhiraleela	Mandankula Road	077 8449170	2	0	2	9.6859527	80.0633209

Annex 2: Photos of the well recharge system installed in Kopay




Thankaveluitham Kugarasa well and well recharge system

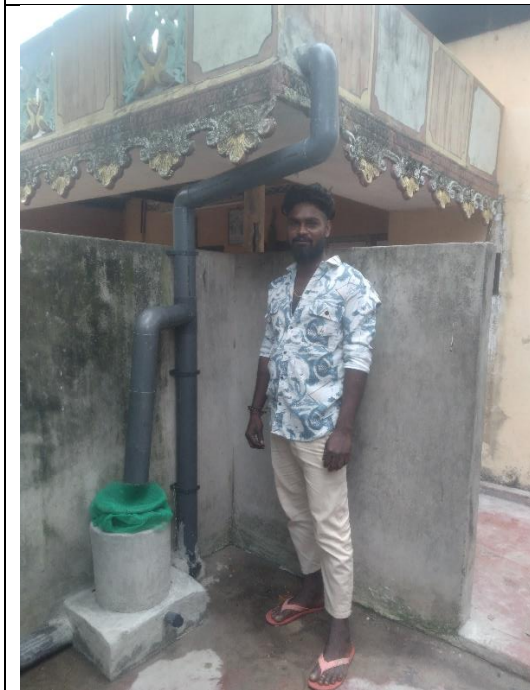

Thevaranjan Kantharaj well and well recharge system



Balasingam Saroja, well and well recharge system

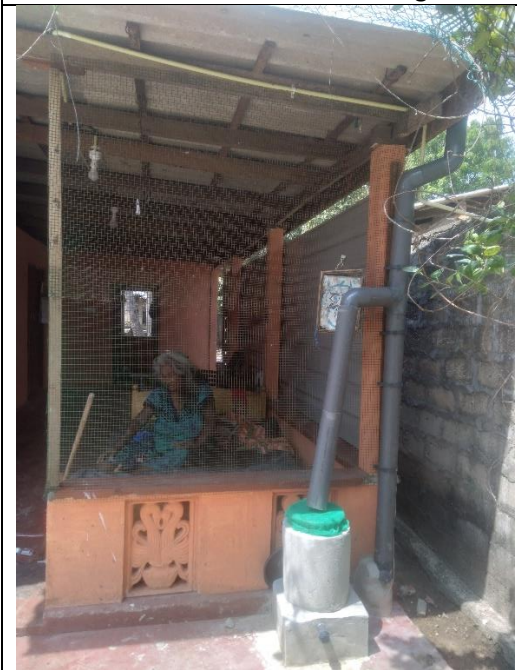

Thusyanthan Renuka well and well recharge system



Ragupathi Kala, well and well recharge system



Vasanthaselan Maliny, well and well recharge system



Kanagalingam Ramesh, well and well recharge system



Sinnathurai Santhakumar, well and well recharge system



Sivarsa Balrasa , well and well recharge system



Senathiraja Santhiraleela, well and well recharge system

Annex 3

Registration of Participants

Program Name: P & M Program

School/Hospital/Organization/Village..... Madathukudy

GN Irupali East..... DSD to Valikamam East Jaffna District : Kurunegala Date 10.02.2026

No	Name නම	Address ලිපිනය	Phone දු. අං	Male පිරිම	Female කුම	Signature අත්සන
1	මහේස්වරිය සෙනරත්	කොළඹ 13	0768853104		✓	U.S.P. 01.02.2026
2	සුමනි සෙනරත්	"	0775949890	✓		U.S.P. 01.02.2026
3	සුමනි සෙනරත්	"	0762562643	✓		U.S.P.
4	සුමනි සෙනරත්	"	0761329725		✓	Kala
5	සුමනි සෙනරත්	"	0766312768		✓	U.S.P.
6	සුමනි සෙනරත්	"	0769935717	✓		U.S.P.
7	සුමනි සෙනරත්	"	-	✓		U.S.P.
8	සුමනි සෙනරත්	"	-	✓		U.S.P.
9	සුමනි සෙනරත්	"	0778449170	✓	✓	U.S.P.
10	සුමනි සෙනරත්	"	0768425827		✓	S.P.
11	සුමනි සෙනරත්	"			✓	U.S.P.
12	සුමනි සෙනරත්	"	0778449170		✓	U.S.P.
13						
14						
15						
16						
17						
18						
19						
20						
